


CARNWATH ROAD RIVERSIDE

Community Liaison Working Group drop-in session
Wednesday 30 November



Tideway

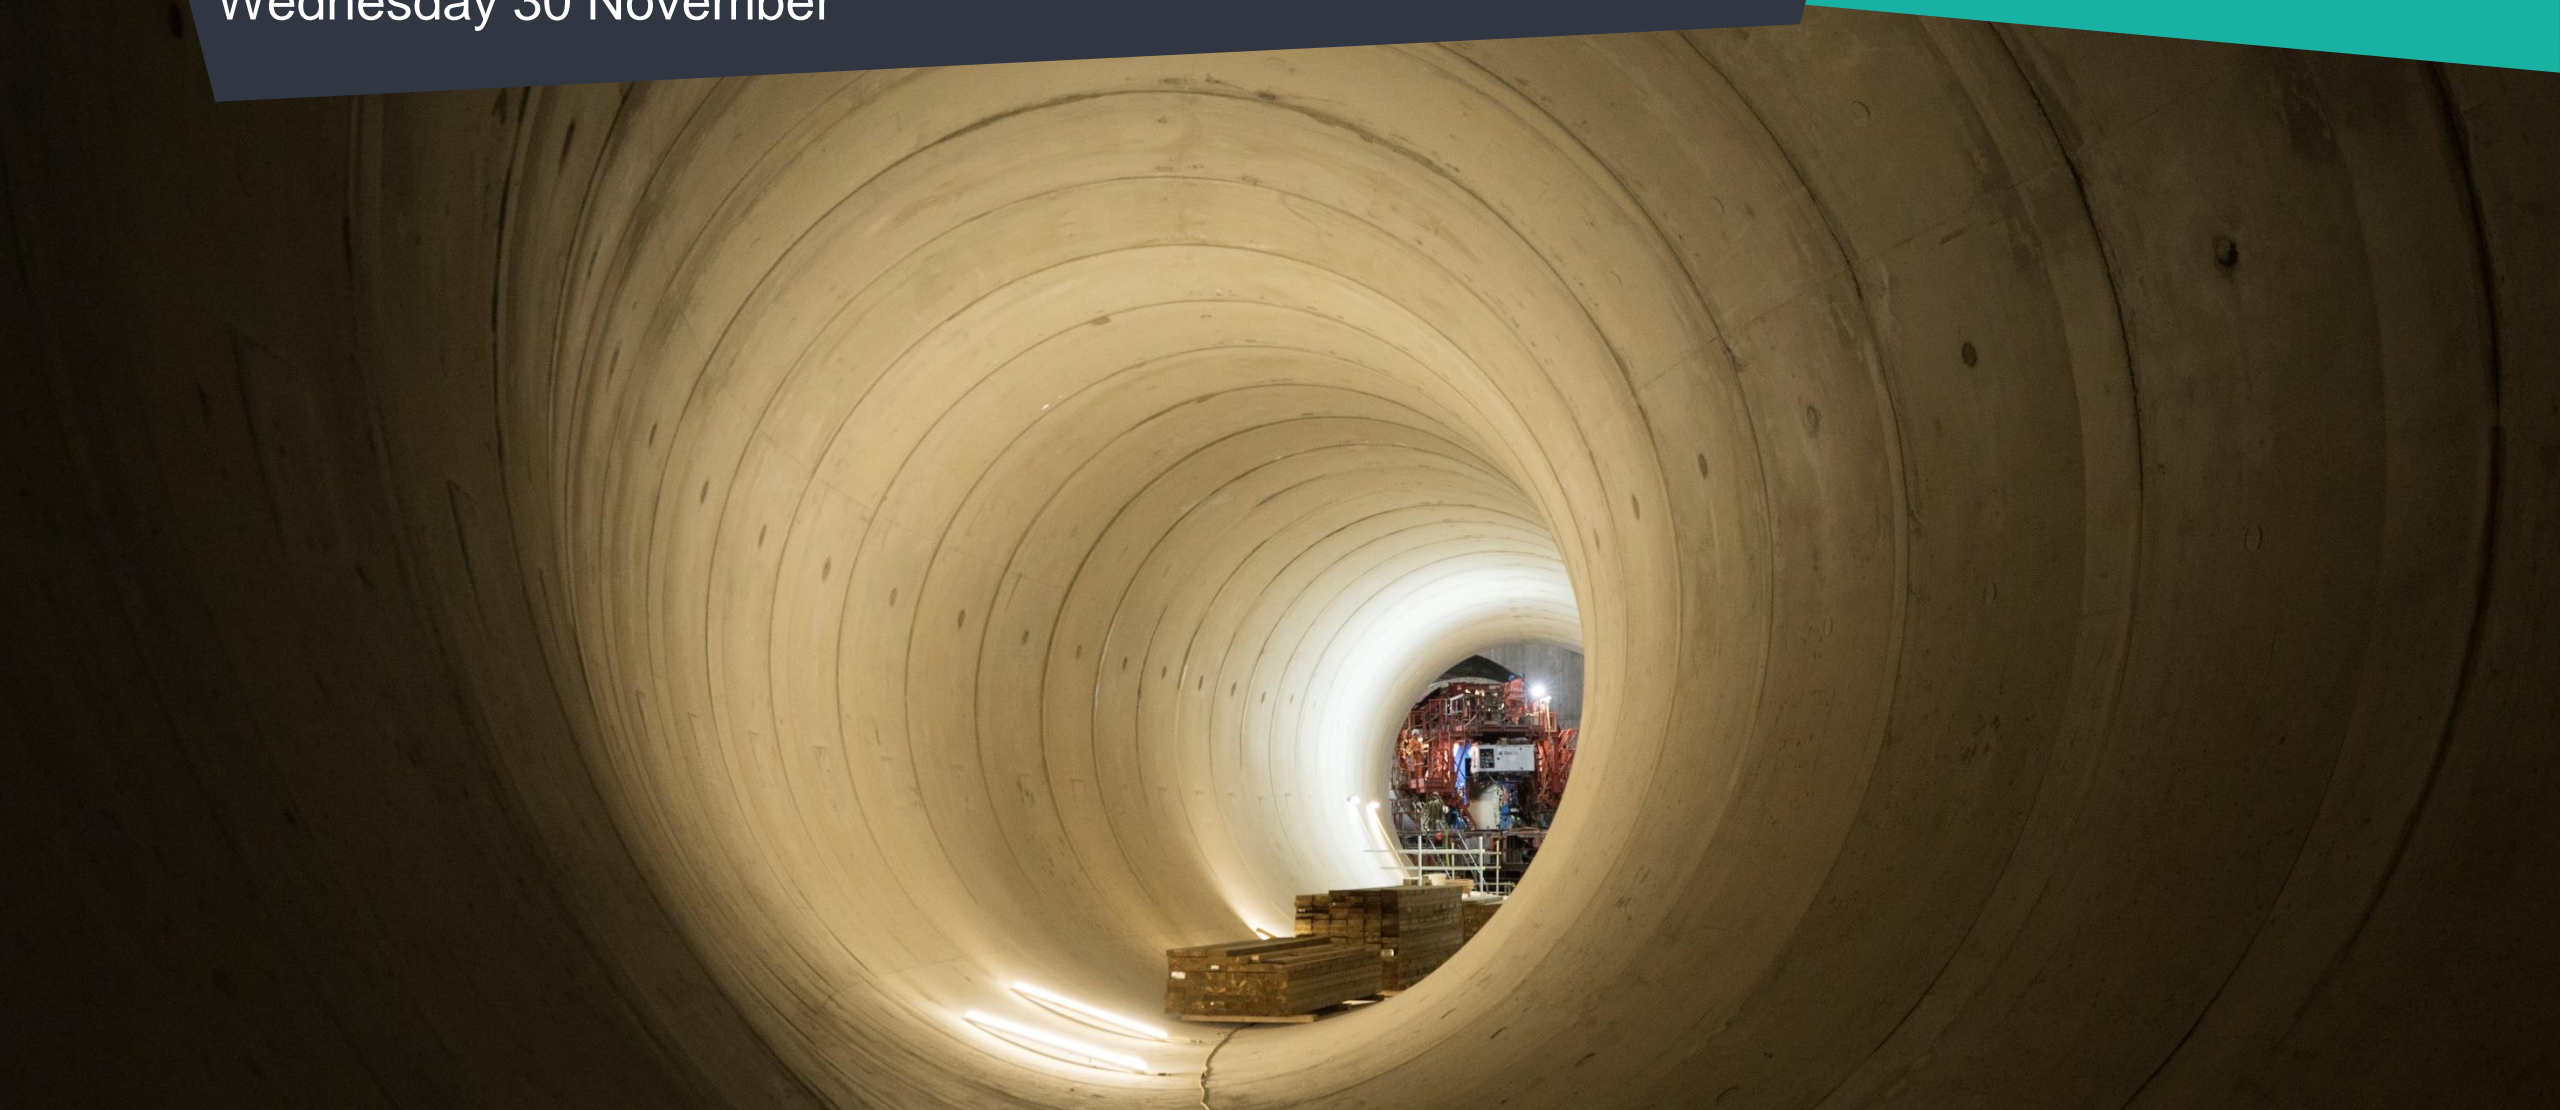



WELCOME




**WORKS
UPDATE**


John Clifton, Section Manager

Main Tunnel Secondary Lining


- 7km of secondary lining completed
- 110000 tonnes of concrete cast.



TIDEWAY WEST C405 - MNTLA		Total Blocks Completed	Total Length Completed	Percentage Complete	Current Leading Block	Concrete Mix	Last Pour Date
SECONDARY LINING PROGRESS		818 / 818	6931.8 m / 6931.8 m	100%	TSL 818	CM4B3.6	20/11/2022
PERI SHUTTER BULKING PROGRESS		5/5	42.76m / 42.76m	100%	TSL 818a	CM4B3.6	29/10/2022

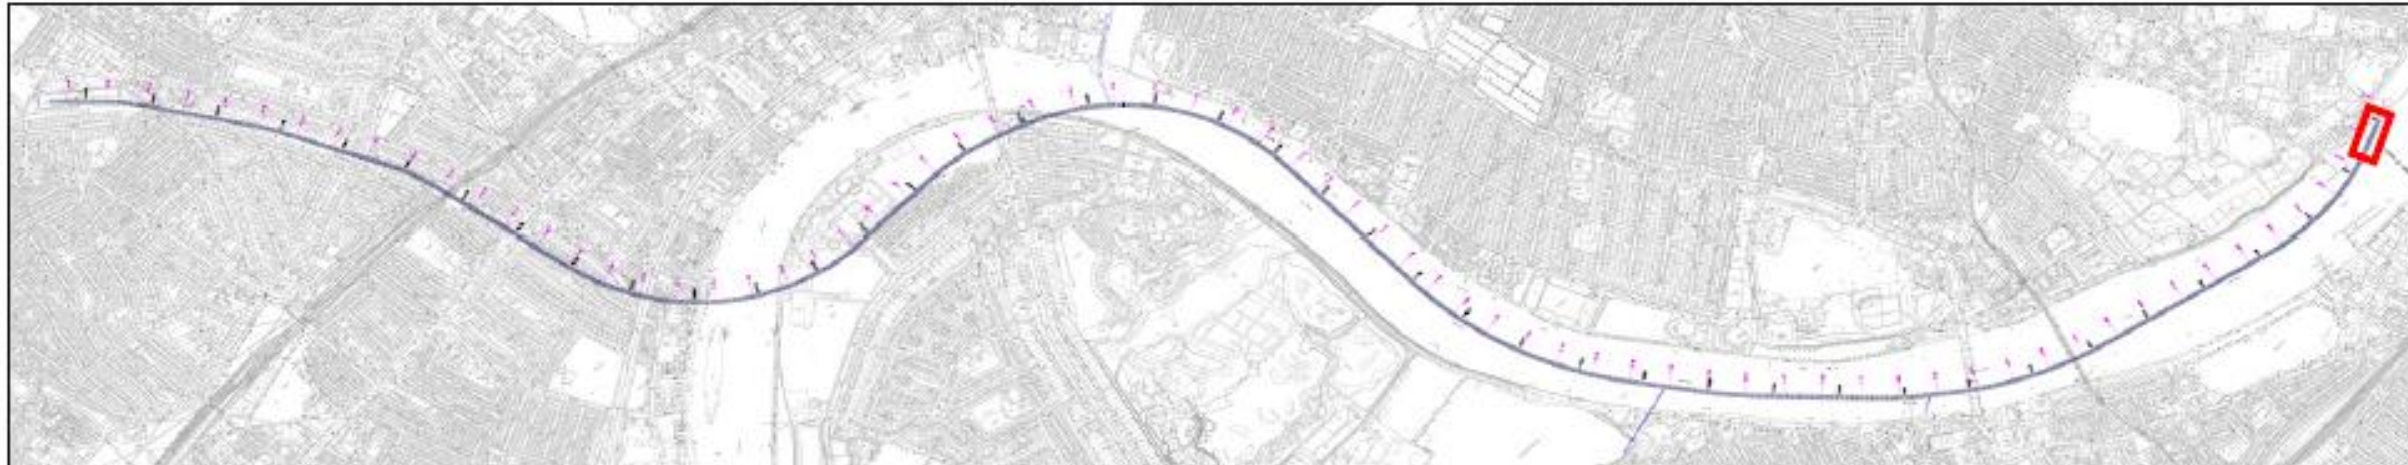


Surface Operations

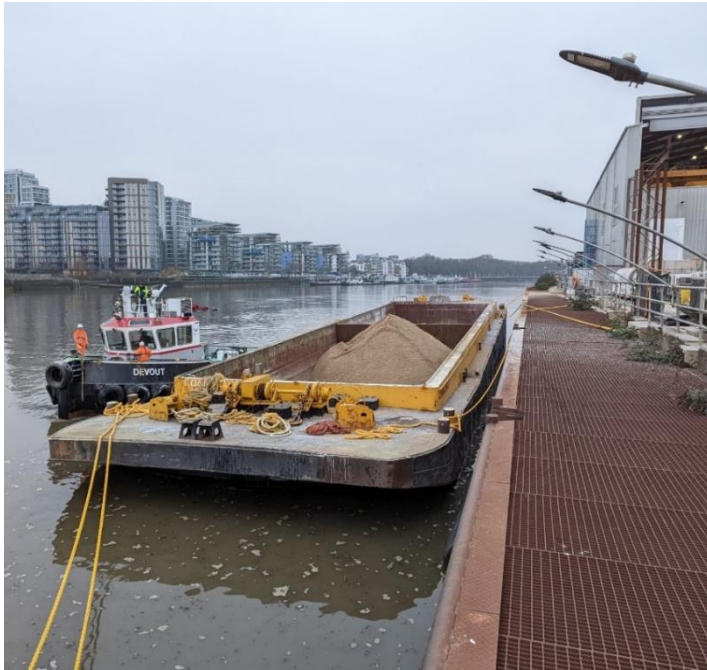

- The berth will be used for moving materials and equipment that is too large to go by road.




- Surface areas on the site will be used to precast elements of the shaft

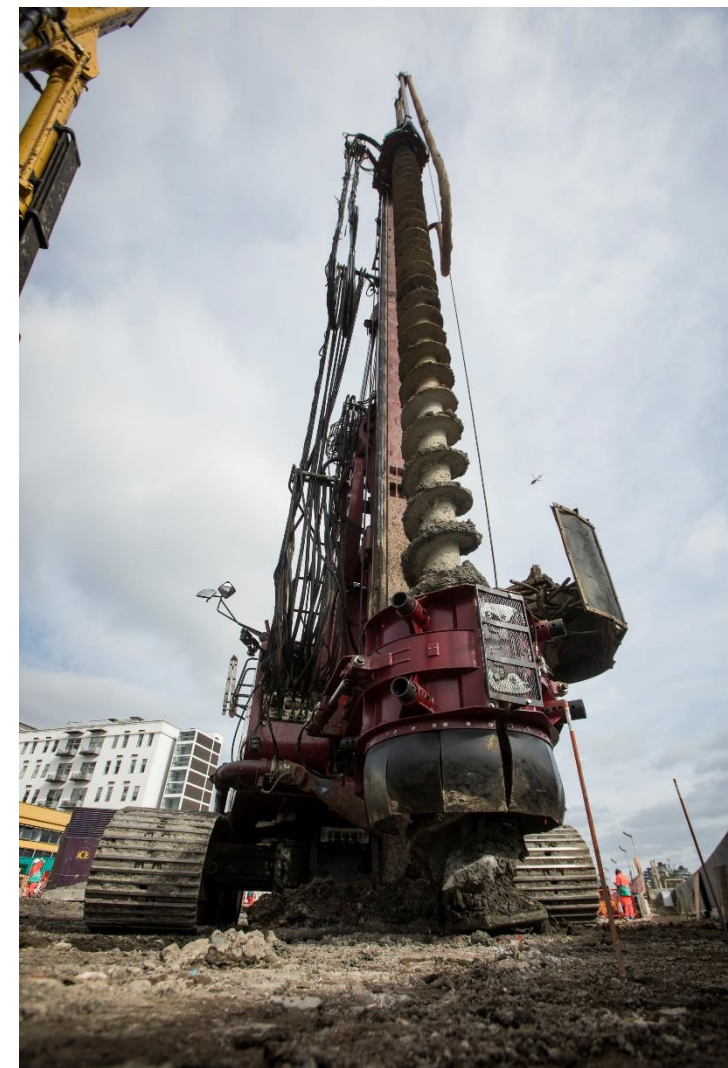


- Piling for the air treatment chamber with 70 piles to be bored at the start of 2023

Current Site Layout

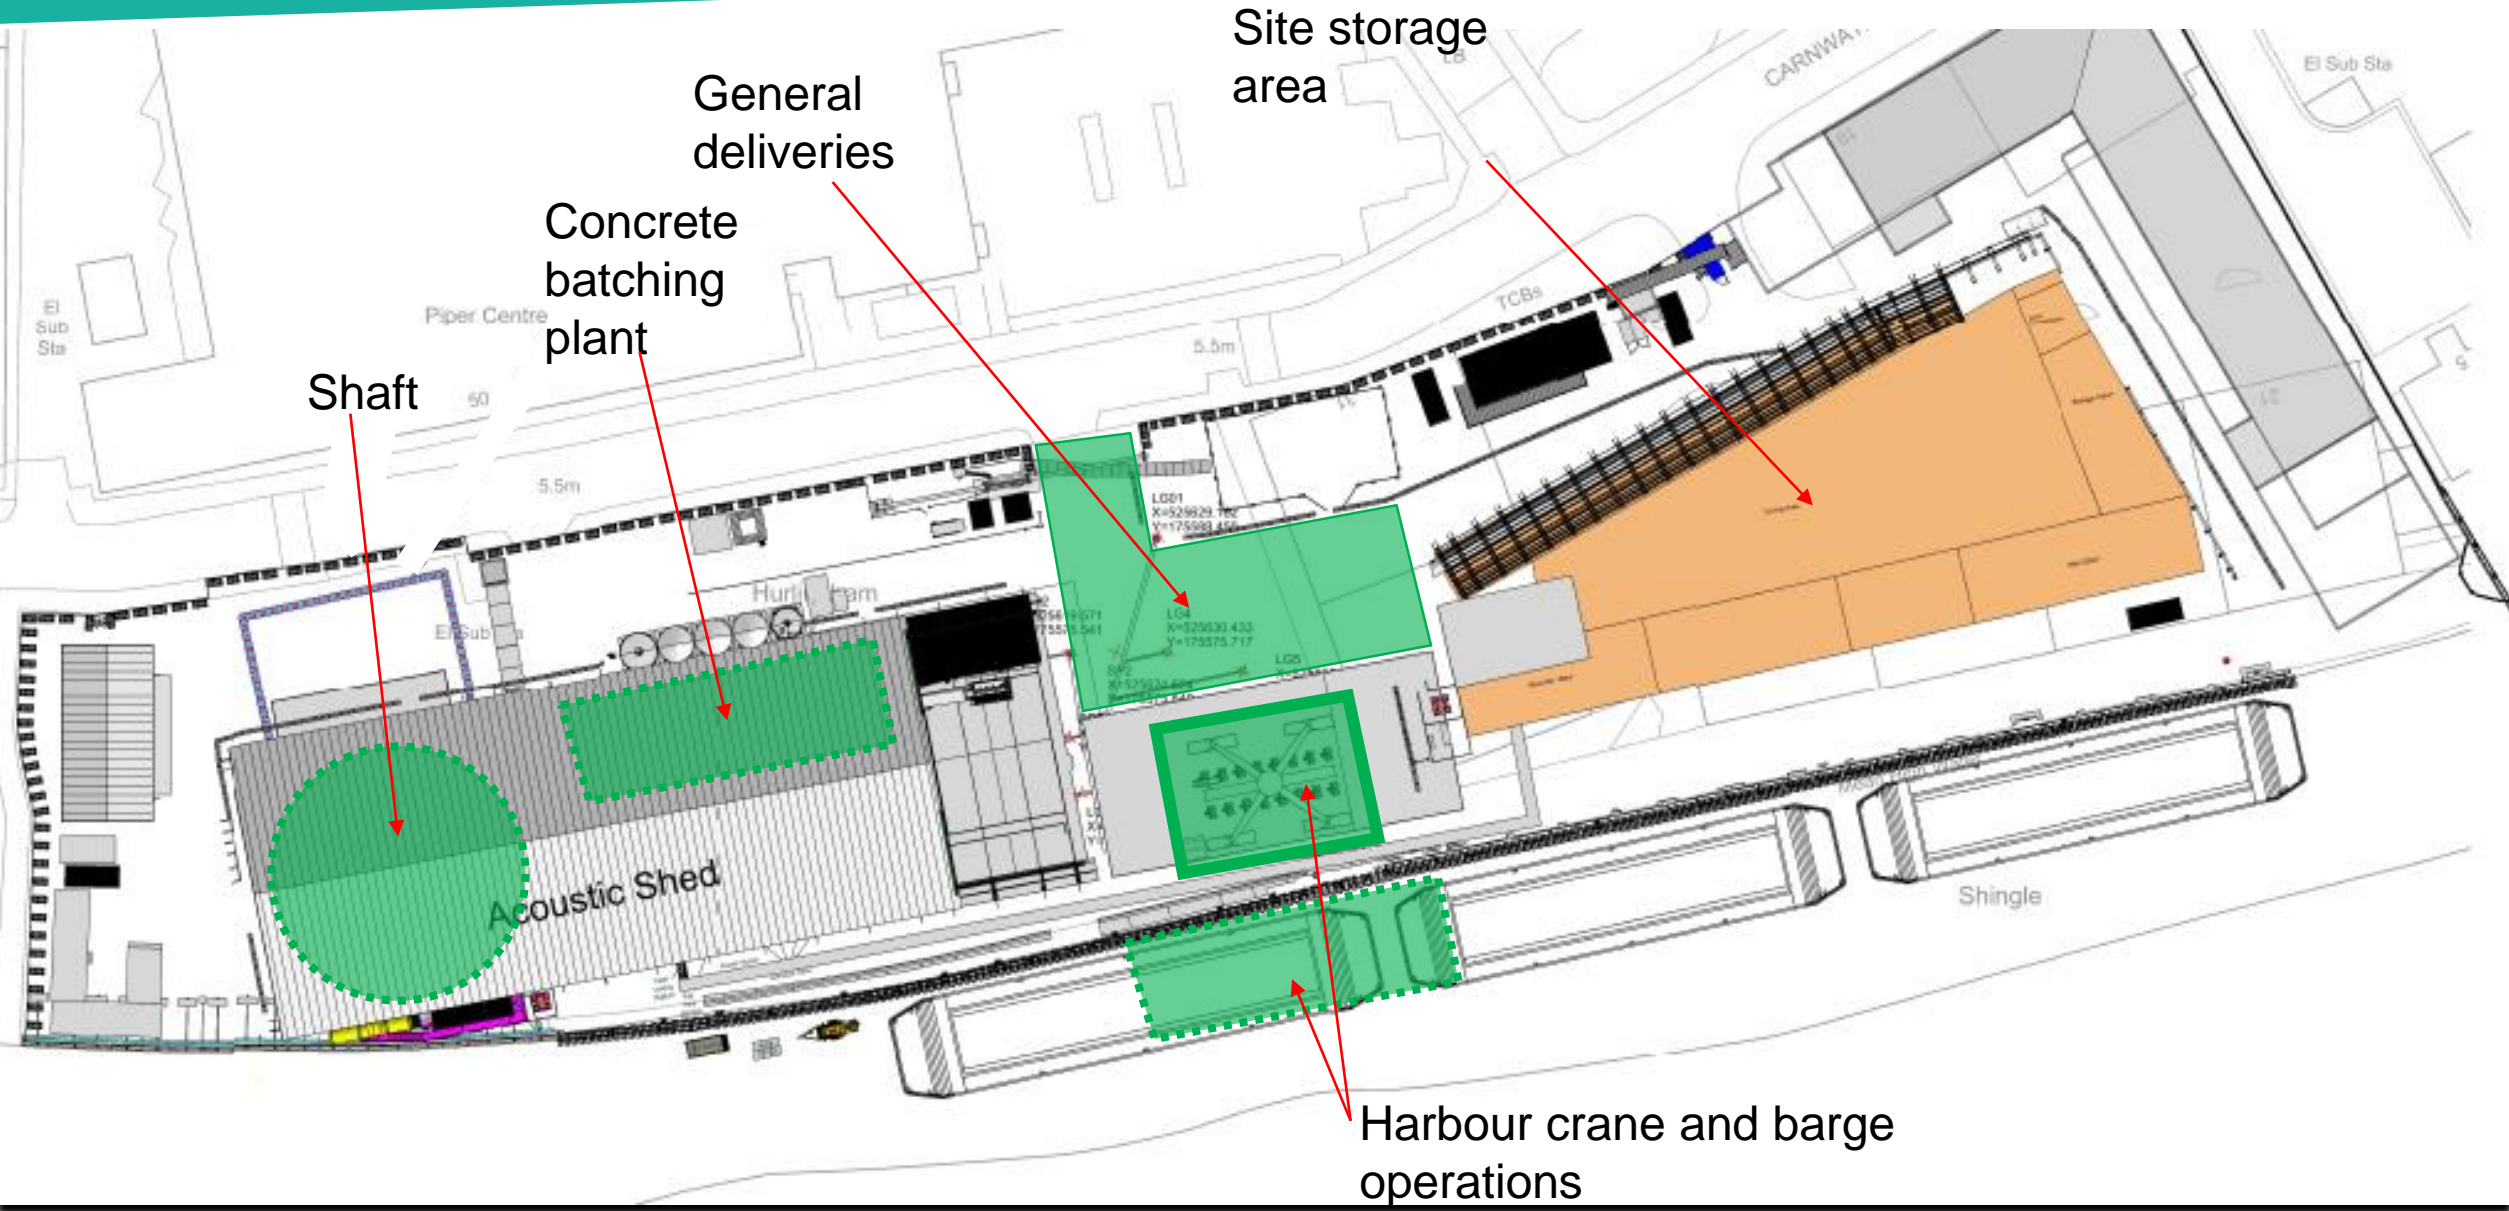

Jan - Feb Site Layout

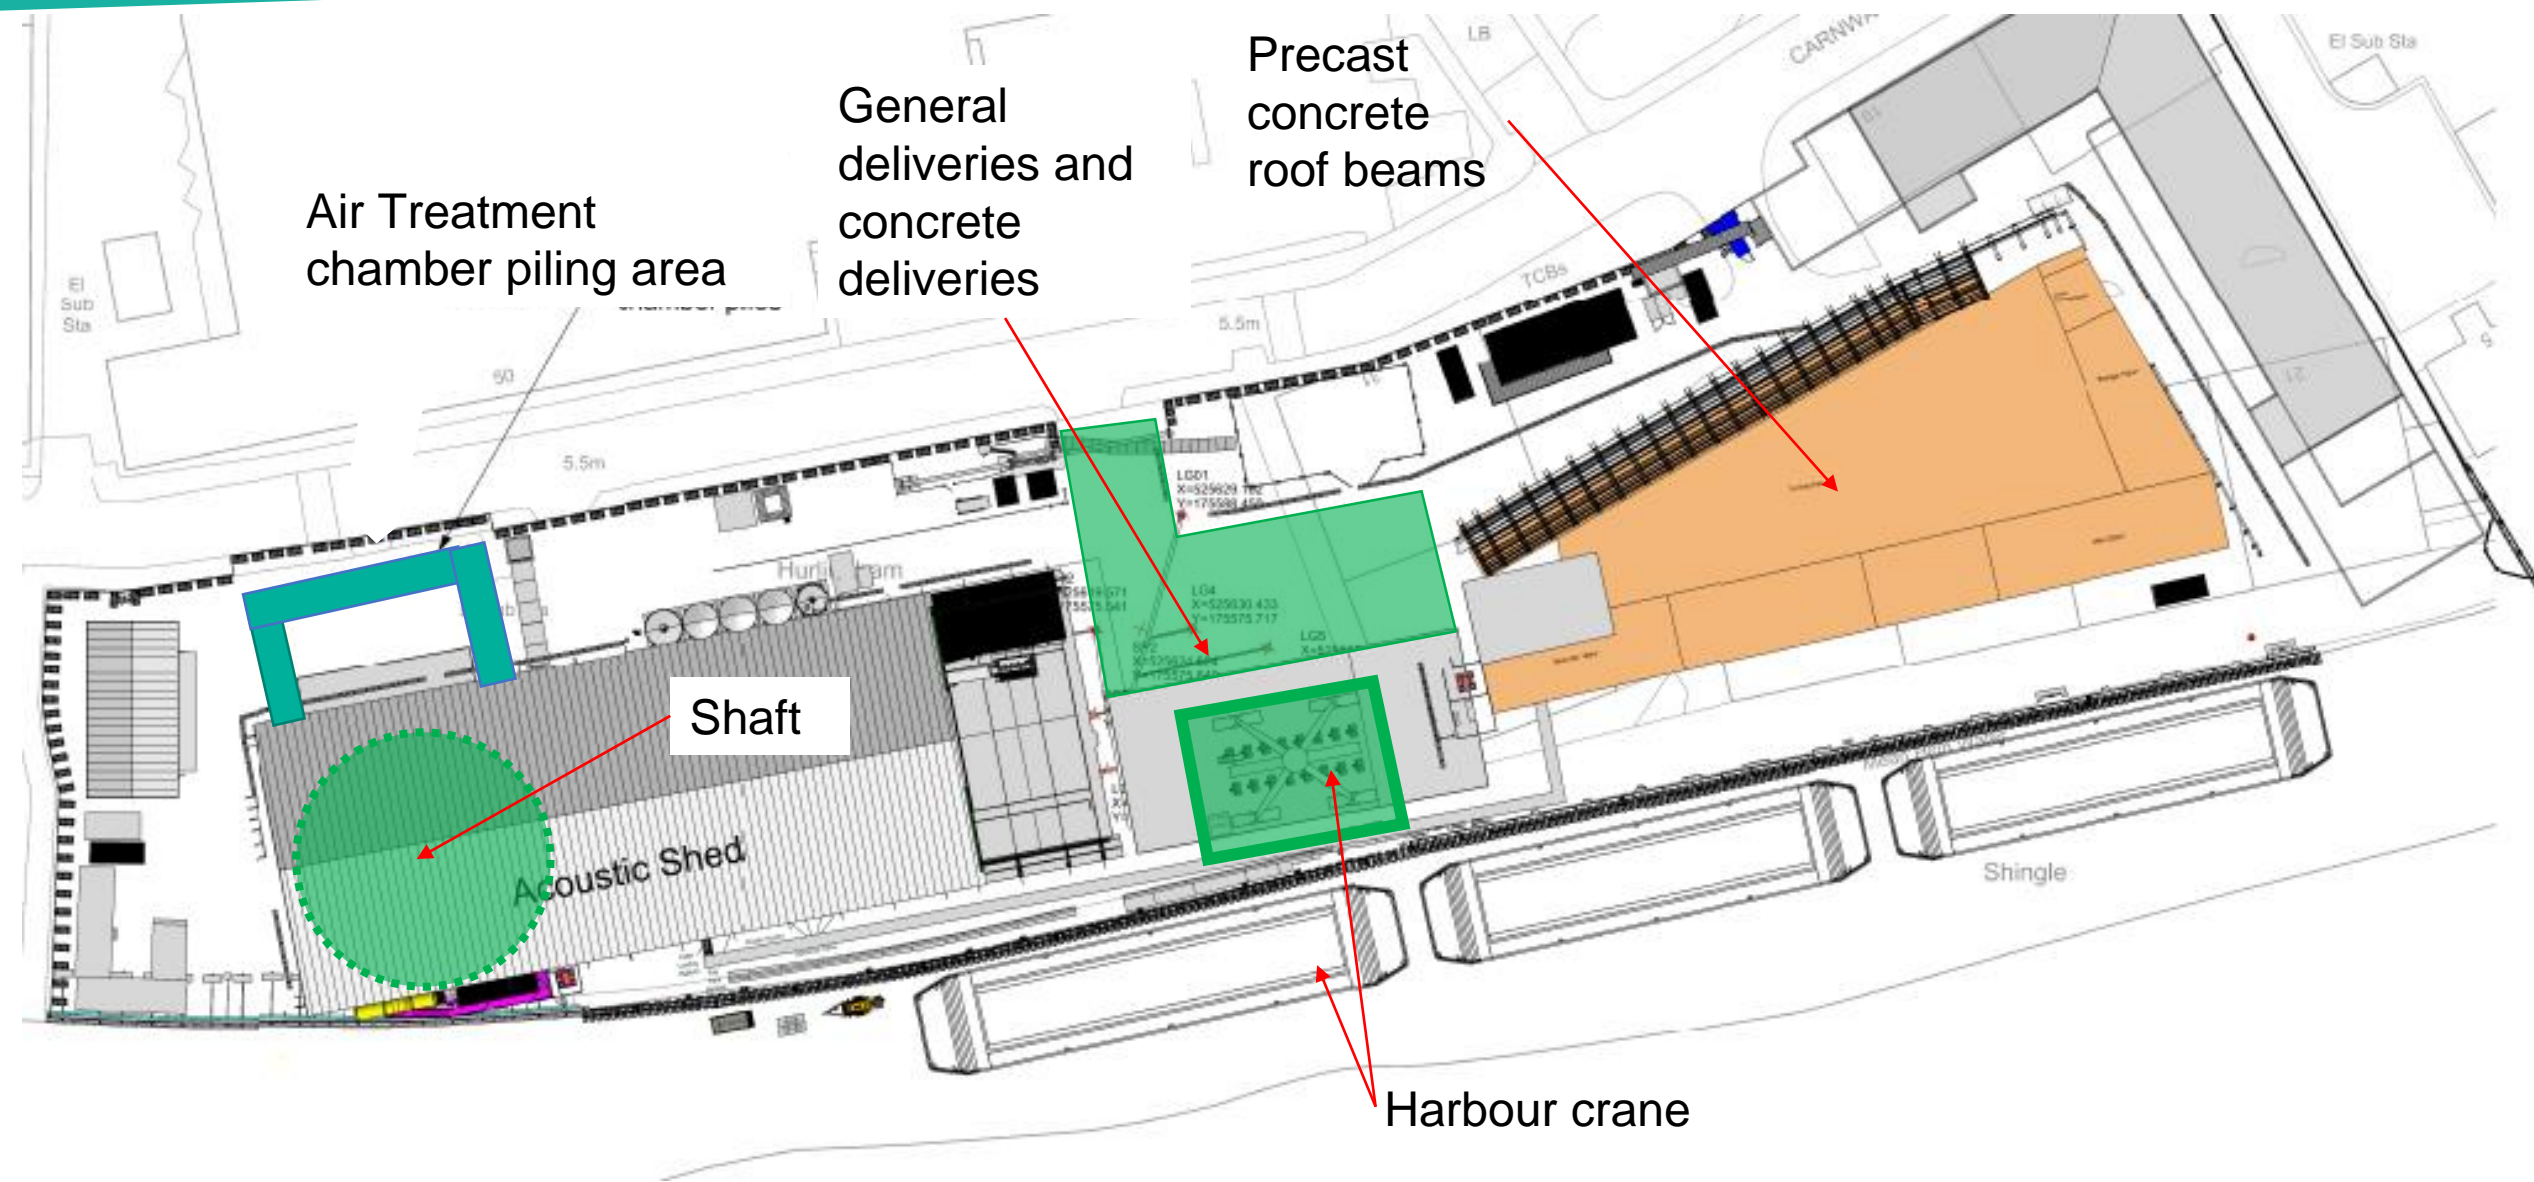


Feb - May Site Layout


Shaft construction works

General deliveries and concrete deliveries


Precast concrete for shaft

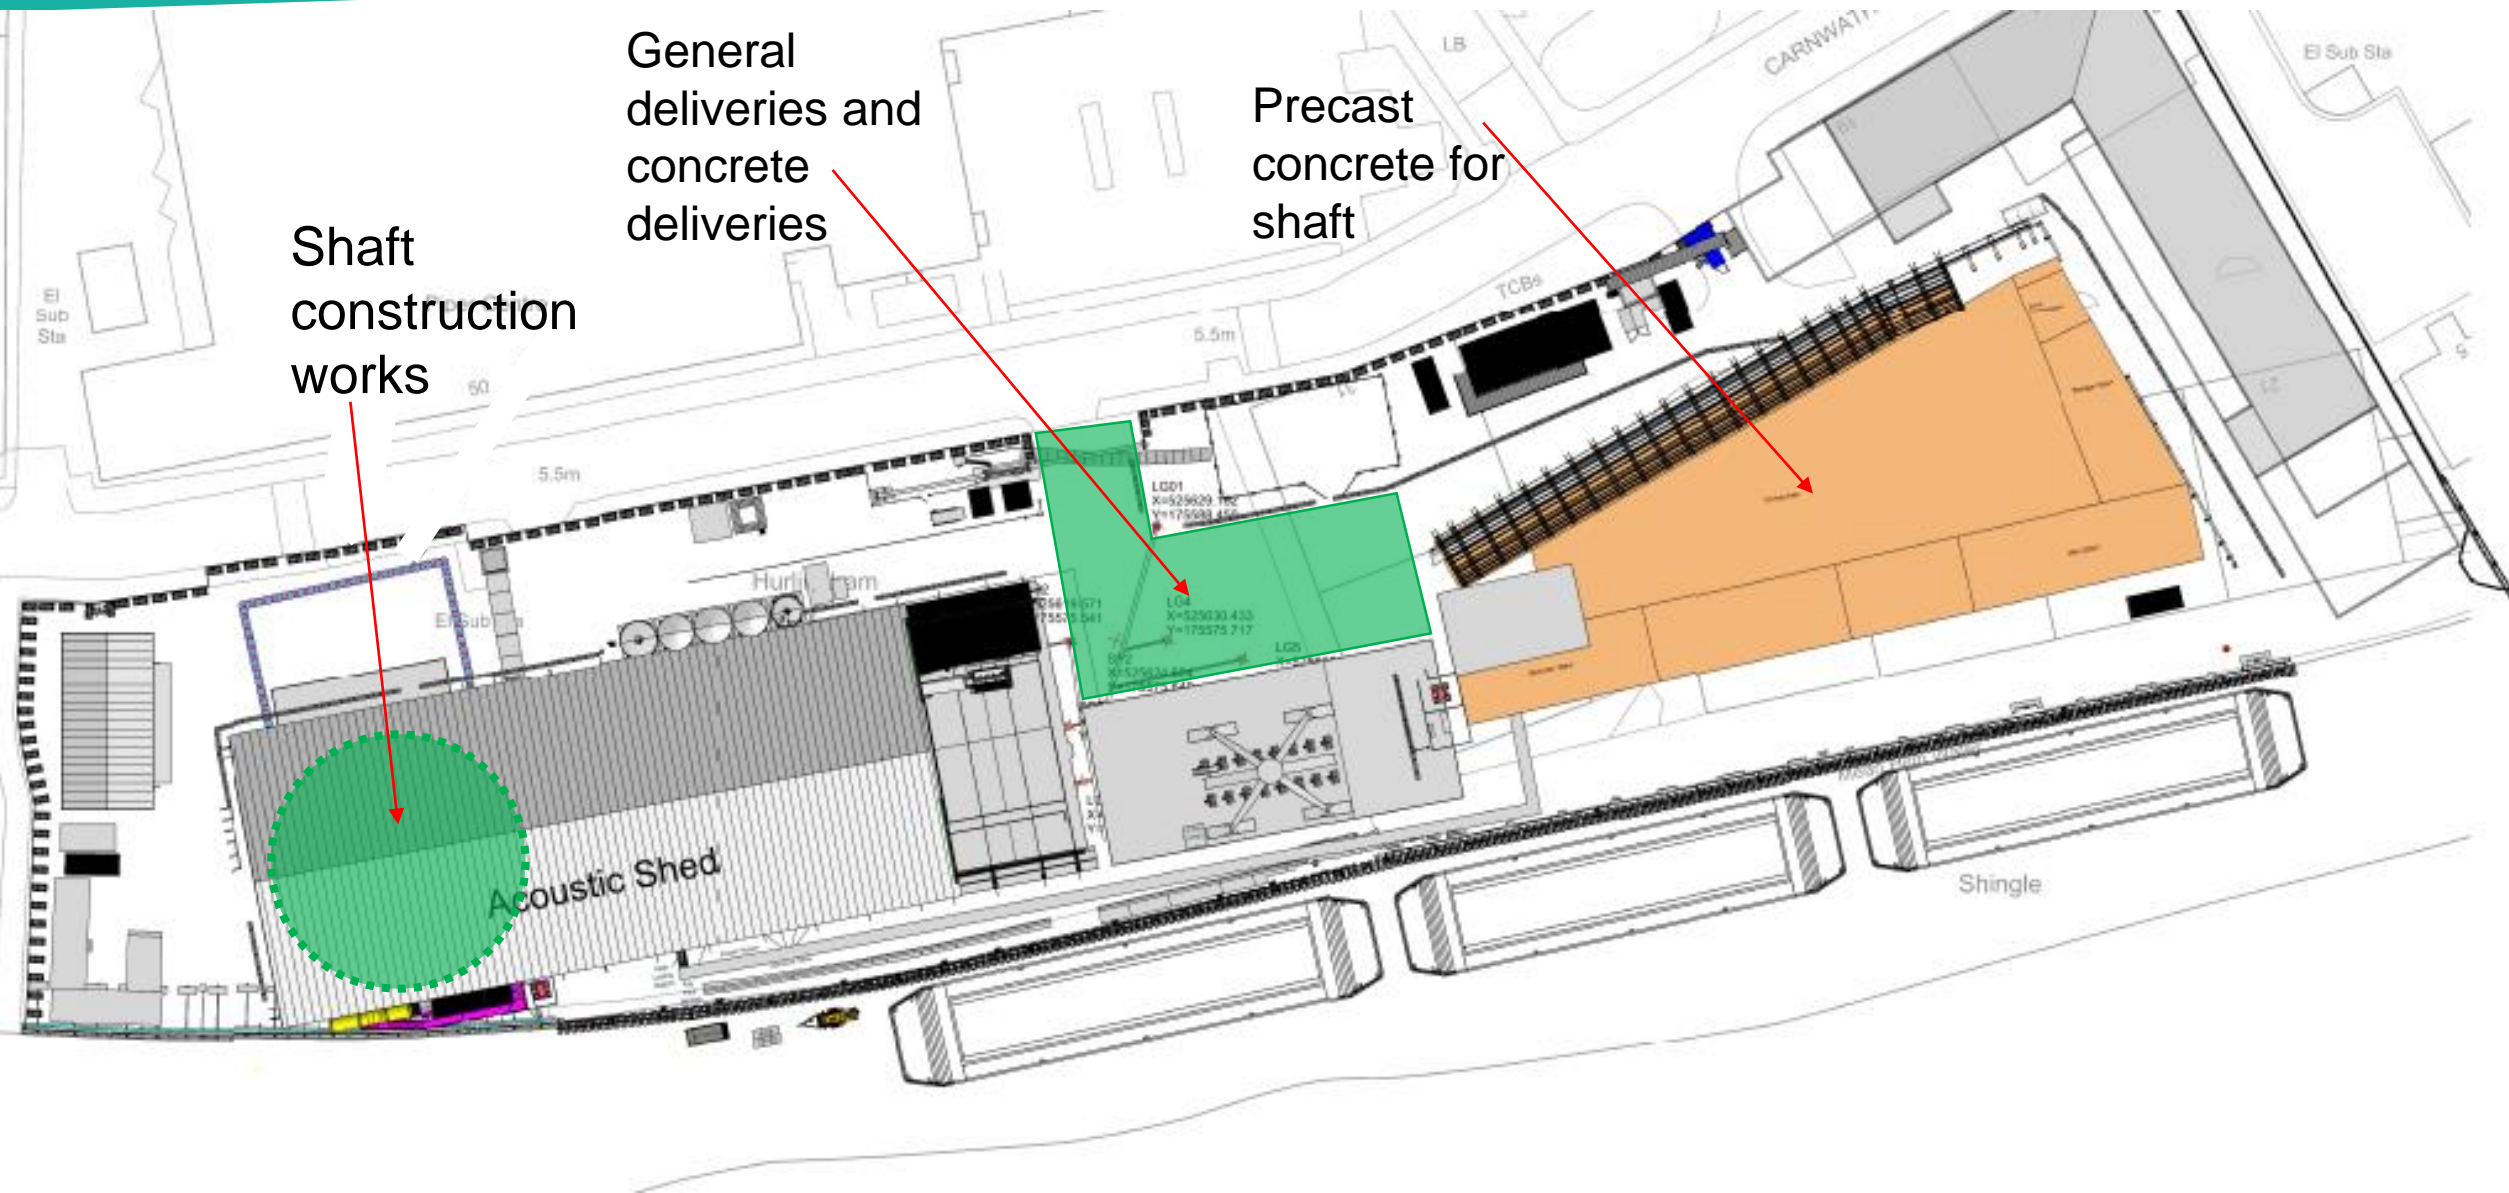

May - June Site Layout

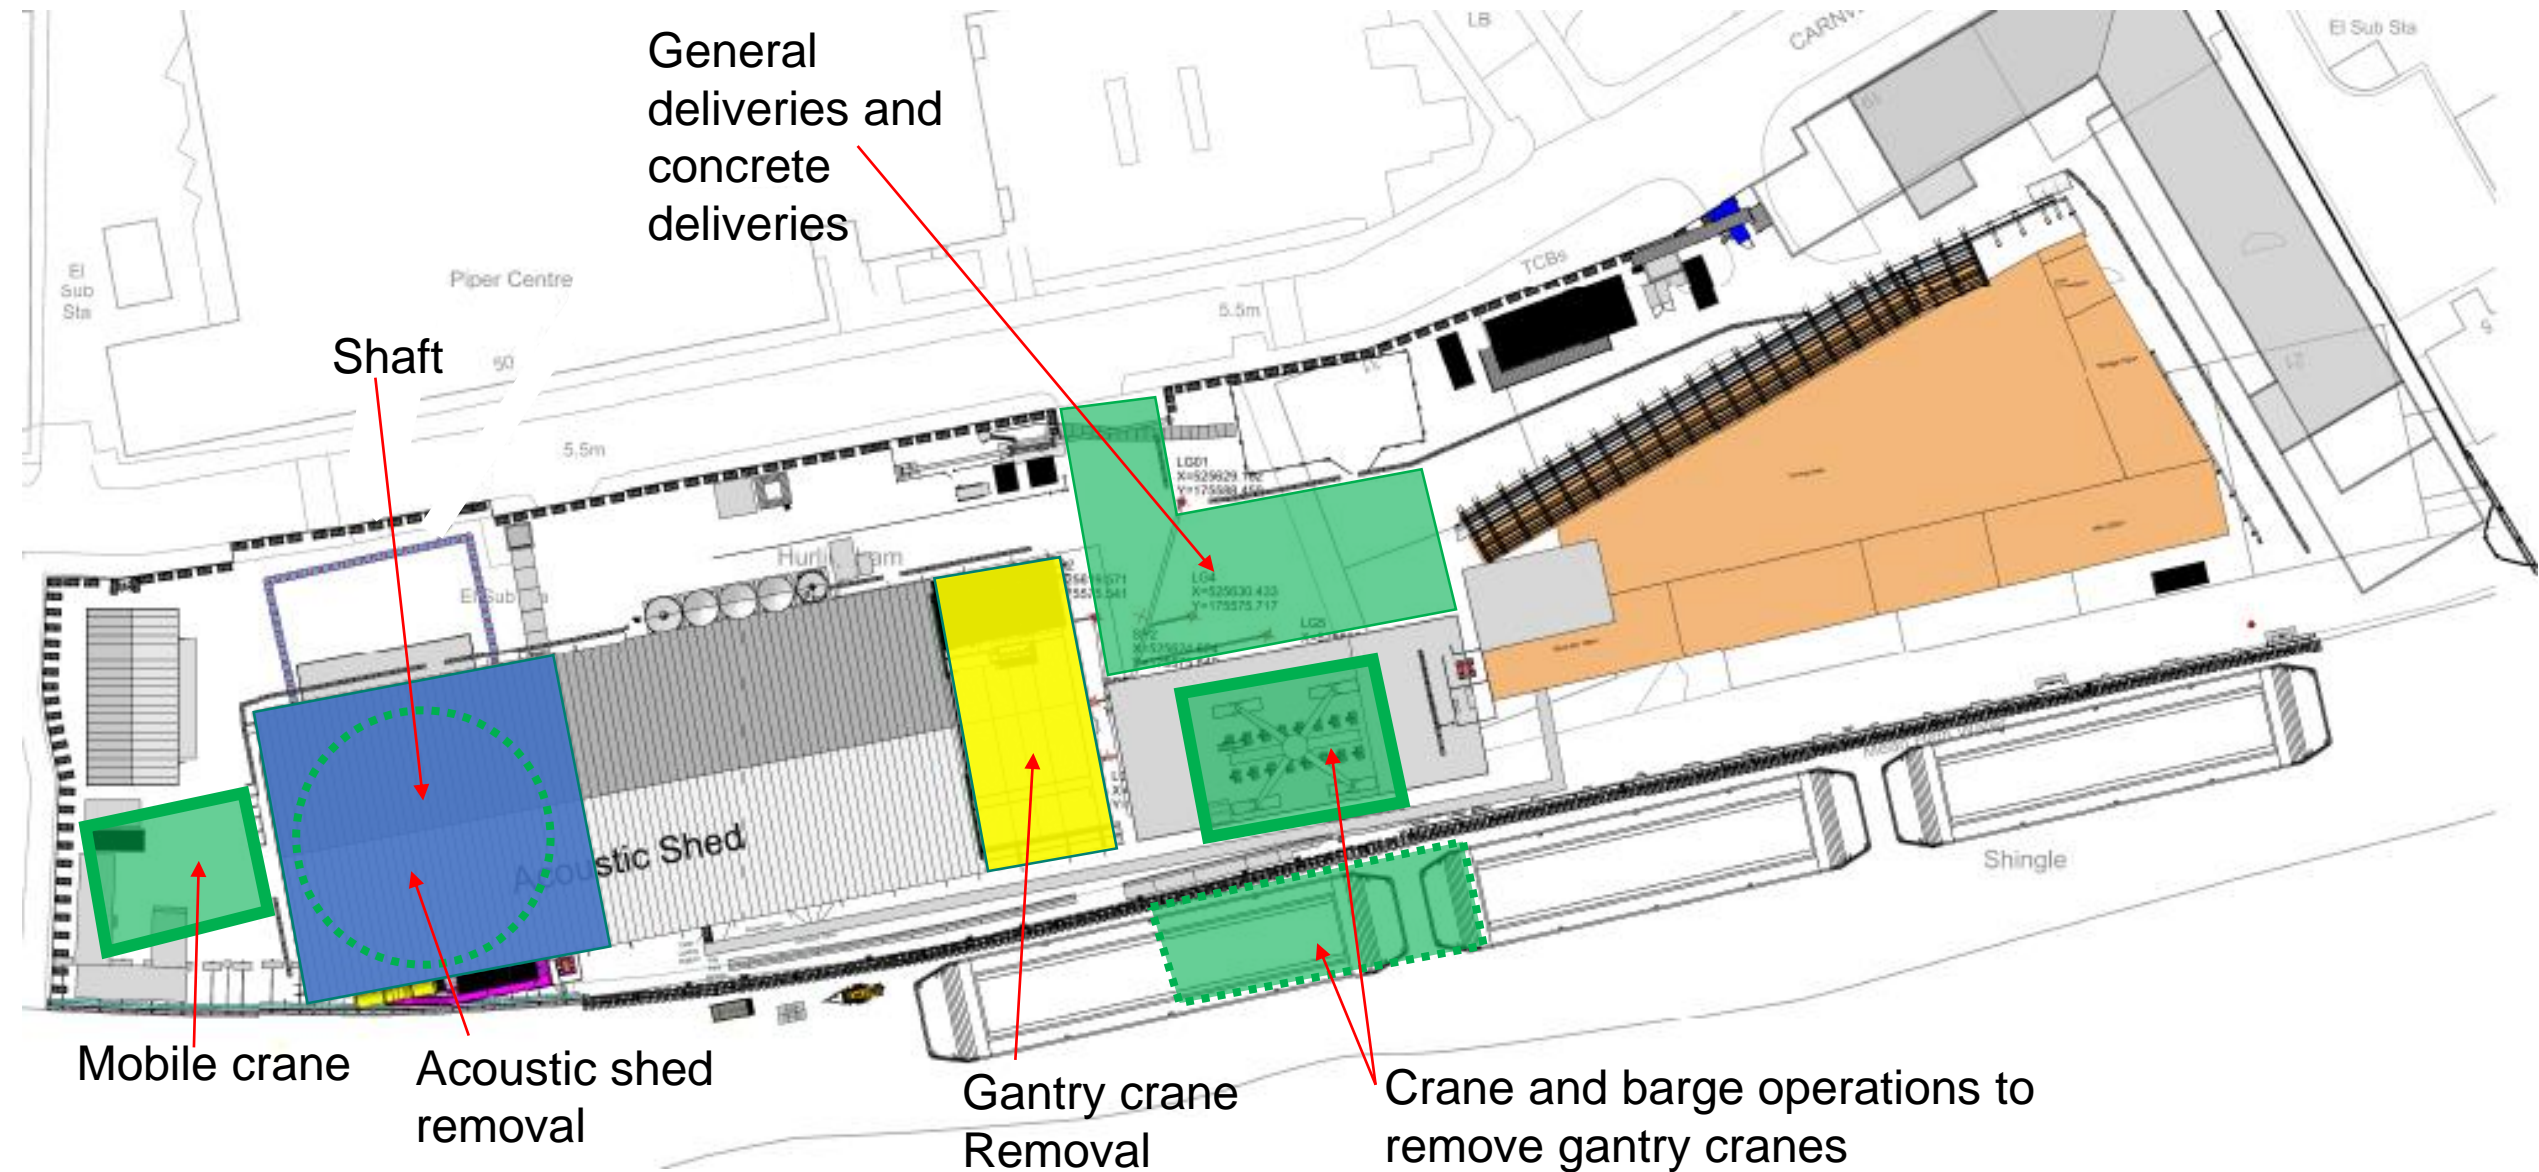

June – July Site Layout

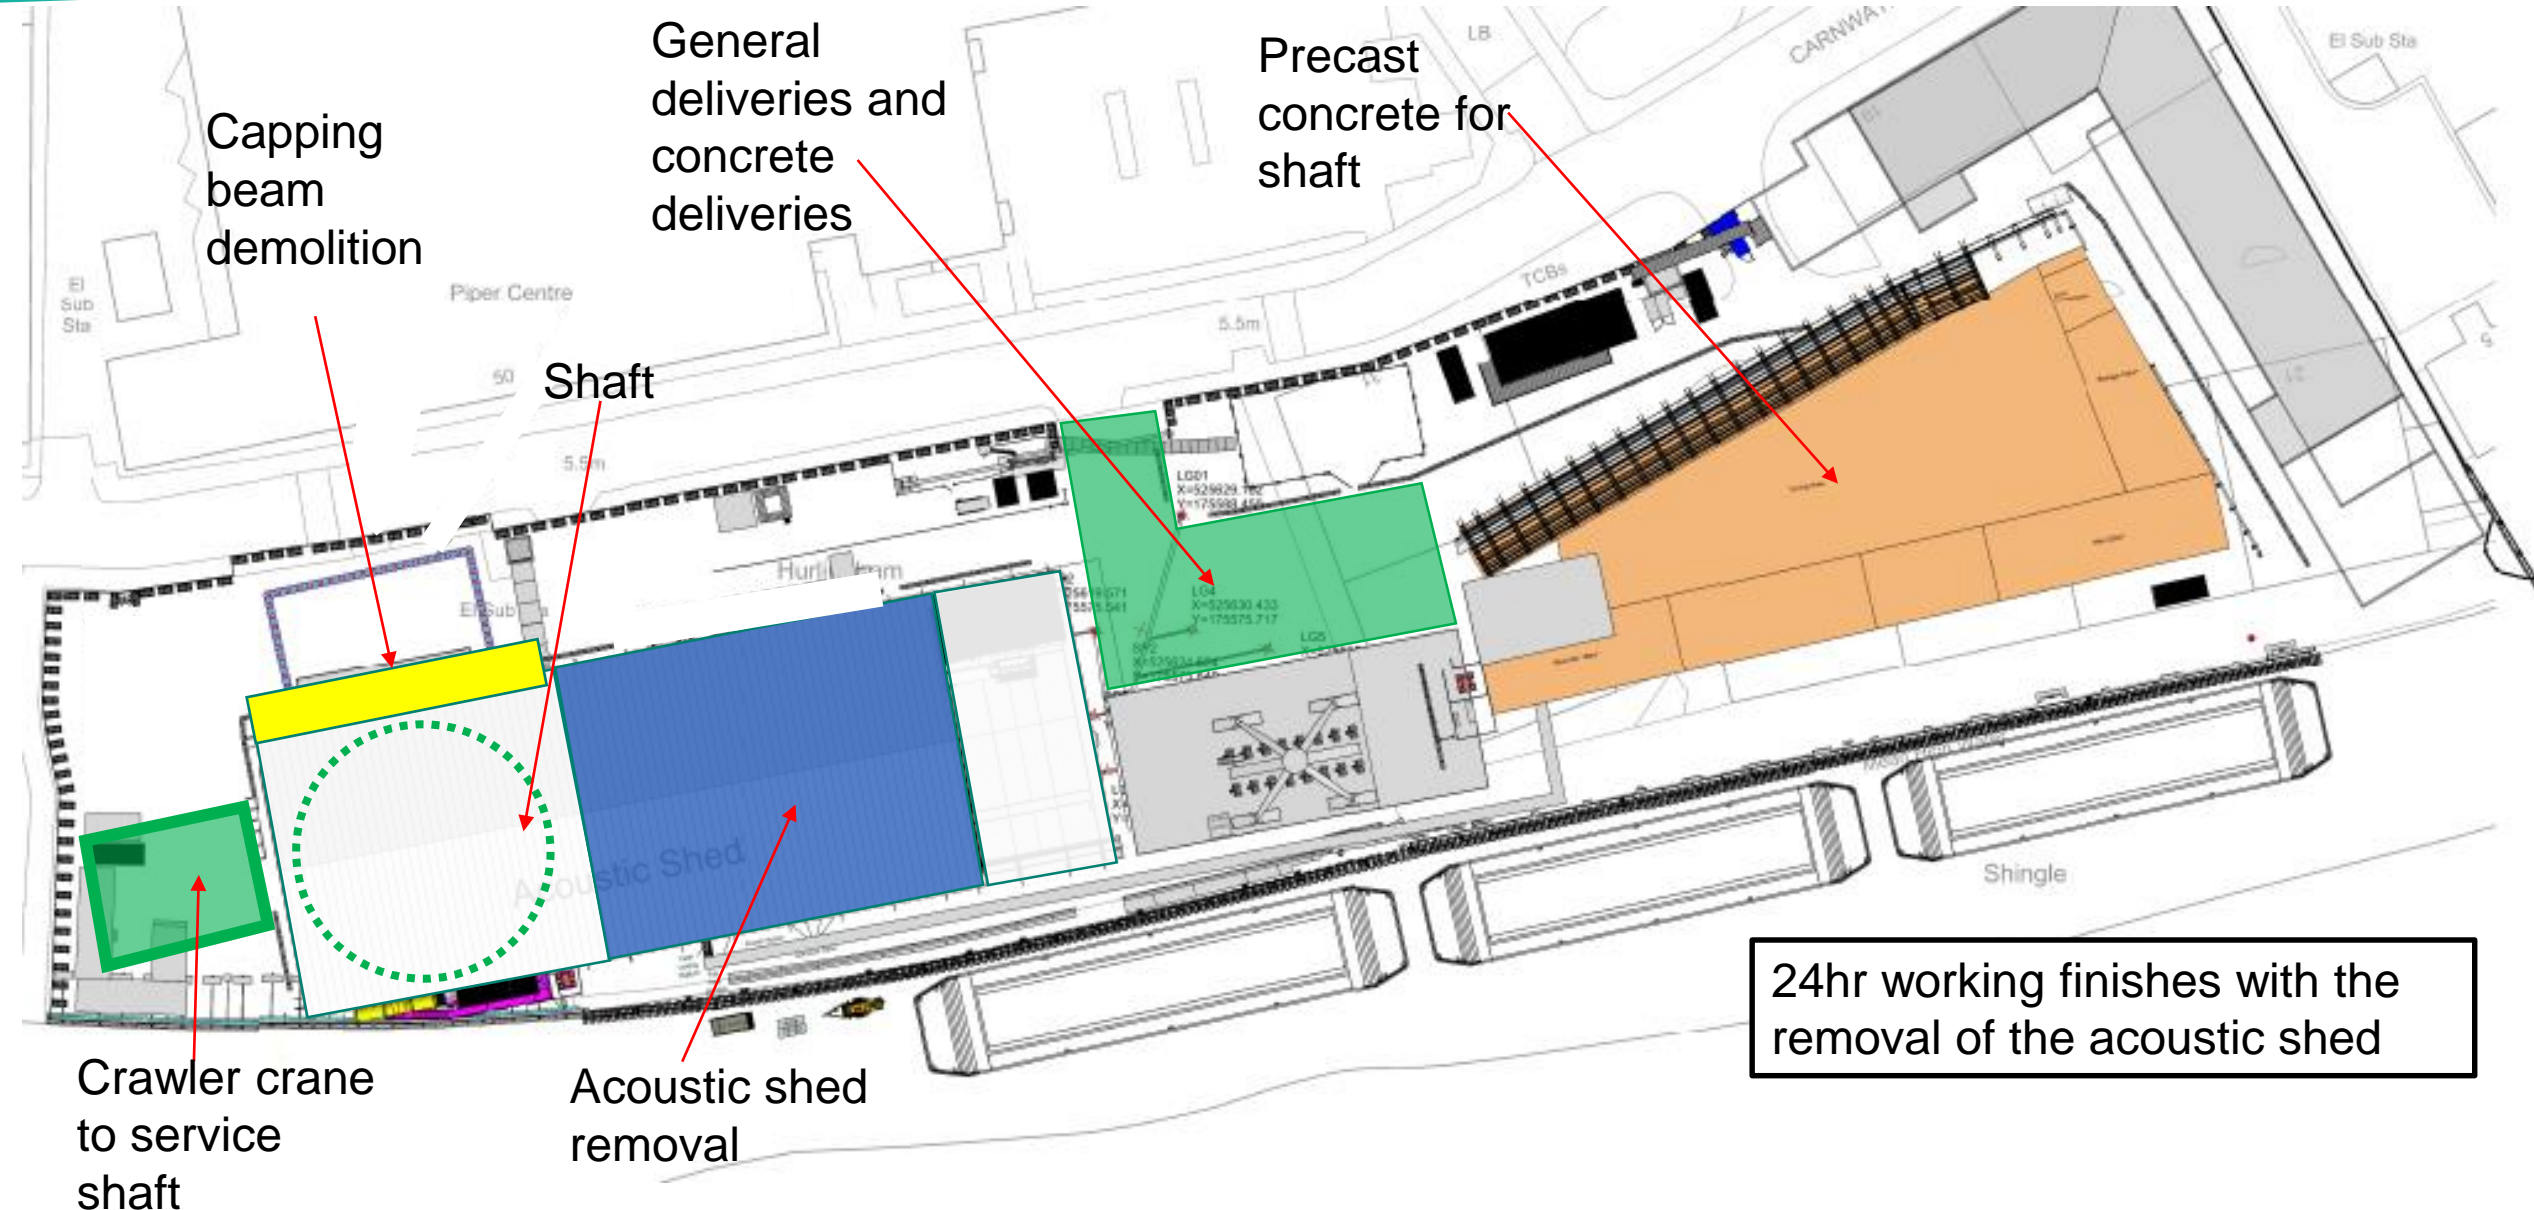

Capping beam demolition

General deliveries and concrete deliveries

Precast concrete for shaft

Shaft

Crawler crane to service shaft

Acoustic shed removal

24hr working finishes with the removal of the acoustic shed

Current programme

Key dates

- Secondary lining completed – November 2022
- Secondary lining demobilisation – November 2022 to January 2023
- Air Treatment Chamber piling January 2023 to February 2023
- Shaft works – February 2023 to September 2023
- Removal of acoustic shed (24hr working finishes) – June 2023 to July 2023
- Surface civil works – July 2023 to January 2024
- Landscaping works – January 2024 to April 2024
- Site demobilisation – January 2024 to August 2024
- BMB vacate site – Autumn 2024
- System testing and commissioning continues until 2024, though minimal on-site activity



Winter site shutdown

The site and site offices will close normal hours on Friday 23 December and will reopen on Tuesday 3 January



**COMMUNITY
ENGAGEMENT**

Katie Ashton, Communications Manager

Complaints / Queries

Since the last meeting we have received the following:

- 23 x general enquiries
- 2 x settlement enquiries
- 30 x noise & vibration complaints
- 1 x traffic complaint
- 1 x commendation



Tideway

Call: 08000 30 80 80

Email: helpdesk@tideway.london

Write to: Freepost TIDEWAY

ICP Cases: February 22 – July 2022

8 claims made in period since February 2022 for Carnwath Road

- 5 awarded
- 1 award extended
- 1 deferred
- 1 not awarded

How To Make A Claim if Affected By Tideway's Work

Who do I go to for advice?

- For personal assistance contact our Helpdesk: 08000 30 80 80 or helpdesk@tideway.london
- For independent advice contact Independent Advisory Service (IAS) Helpline: 0800 917 8845 or info@tidewayias.co.uk

Independent Compensation Panel

You can download an application form from the Tideway website:

www.tideway.london/help-advice/compensation-information/Independent-Compensation-Panel

The Helpdesk can submit your application to the Independent Compensation Panel (ICP) on your behalf or you can submit your form directly to the ICP: admin@tidewayicp.london

Community Investment

- Our community support activities are continuing
- Please contact us if you are aware of an opportunity or community group that we could possibly help



SEAPIA

SANDS END ASSOCIATED PROJECTS IN ACTION

TIDEWAY UPDATE

Emily Black, Engagement Manager

PROJECT OVERVIEW



BMB WEST		FLO CENTRAL		CVB EAST		Thames Water	
Tideway		Tideway		Tideway		Thames Water	
1	Acton Storm Tanks	8	Falconbrook Pumping Station	17	Chambers Wharf	16	Shad Thames Pumping Station
2	Hammersmith Pumping Station	9	Cremorne Wharf Depot	18	Earl Pumping Station	22	Bekesbourne Street
3	Barn Elms	10	Chelsea Embankment Foreshore	19	Deptford Church Street	24	Beckton Sewage Treatment Works
4	Putney Embankment Foreshore	11	Kirtling Street	20	Greenwich Pumping Station		
5	Dormay Street	12	Heathwall Pumping Station	21	King Edward Memorial Park Foreshore		
6	King George's Park	13	Albert Embankment Foreshore	23	Abbey Mills Pumping Station		
7	Carnwath Road Riverside	14	Victoria Embankment Foreshore				
		15	Blackfriars Bridge Foreshore				

MAP KEY			
● (Orange)	Main tunnel drive tunnel site	▬ (Green)	Main tunnel
● (Black)	Main tunnel reception site	⋯ (Dotted Green)	Connection Tunnels
● (Teal)	CSO site	▬ (Black)	Lee Tunnel
● (Light Teal)	Short connection tunnel drive site	◀▶ (Black)	Proposed drive direction
● (Yellow)	Long connection tunnel drive site	● (Purple)	West works site
○ (White)	System modifications	● (Yellow)	Central works sites
		● (Red)	East works site

Latest progress across the project

- Primary tunnelling is now complete
- All shafts fully excavated
- Secondary lining due to complete by mid 2023
- Construction to be substantially complete in 2023
- System commissioning to start winter 2023/24
- Project on track to be operational in 2025
- Fully funded for construction phase
- Strong social and environmental legacy with 90 per cent of commitments on track





Tideway

RECONNECTING LONDON WITH THE RIVER THAMES

#SuperSewer

www.tideway.london
